



DeKalb County Jail Expansion


March 7, 2017 Project Status Update

Project Status & Progress Update

- Submittal & RFI (Requests for Information) review ongoing
 - Fire protection shop drawings have been submitted to the City
 - Revised Fire Alarm shop drawings per RFP's will be submitted to the City in two weeks
 - 121 RFI's have been submitted to date
 - Submittals are 95% complete
- To date 53 Request For Pricing (RFP's) and 19 Architects Supplemental Instructions (ASI's)
- Steel & Precast erection are nearly complete
- Decking & detailing continue
- Opening cut in precast at tie-in to PSB
- Concrete slabs placed in basement & 1st floor west sides
- West half of building backfilled
- Roof drains & storm piping tied in to city storm sewer
- Storm & sanitary sewer work outside the foundation now 85% complete

Progress Update Continued...

- Water service extended into building
- Roof blocking & temporary roof installation underway
- Overhead Electrical & Plumbing work continued in the basement
- Hanger inserts, sleeves, drains, etc. have been installed throughout west half of building in preparation for slab pours

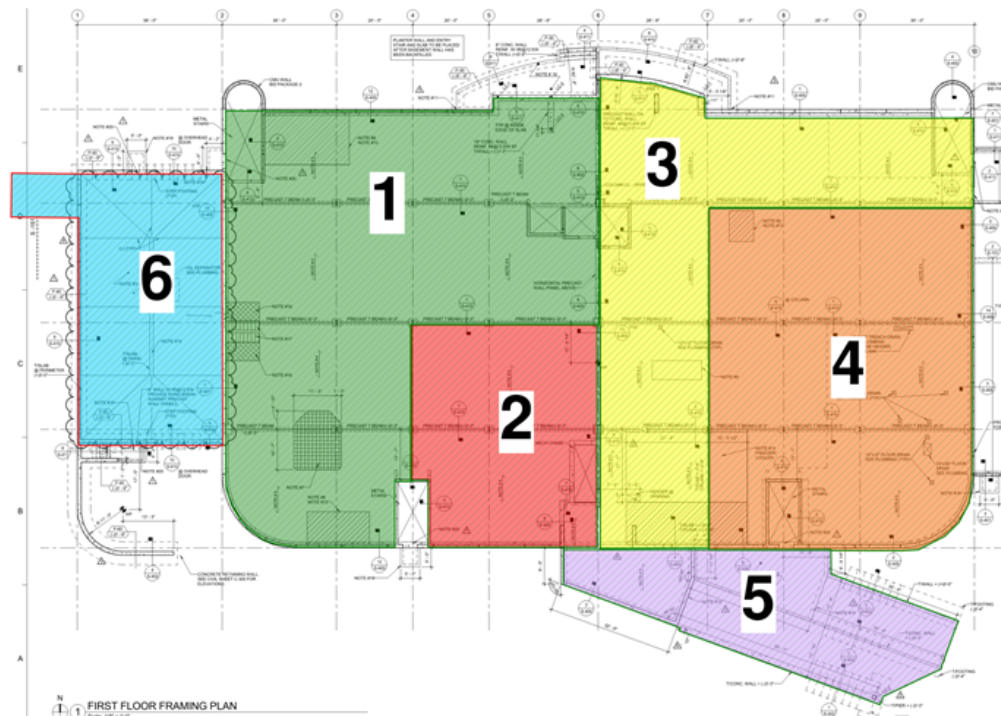

Upcoming Work Activities

- Precast & steel detailing to wrap up mid March
- Sallyport & bridge precast & steel early March
- Concrete slab pours on level 2 & 3 west then following to the east side
- Overhead plumbing & electrical continue
- Fire protection install will start in basement
- Underground plumbing & electrical install in the basement
- Remaining foundation backfill following 1st floor east slab pour
- Exterior metal stud framing to start in March
- Spray fireproofing & interior masonry starting late March
- 2nd Floor Mockup Cell to be built early April
- Plumbing in-wall rough in will start on 1st floor in March
- Major overhead MEPFP rough in to start in April following masonry
